



Project Pampafos Três Estradas DBPlant

November 2025

Três Estradas

❖ Timeline





Três Estradas

❖ Timeline

2025
October

Site mobilization
Construction of access roads
Safety programs





Três Estradas

❖ Timeline

2025
October

Site mobilization
Construction of access roads
Safety programs






Três Estradas

❖ Timeline


2025
October

Site mobilization
Construction of access roads
Safety programs

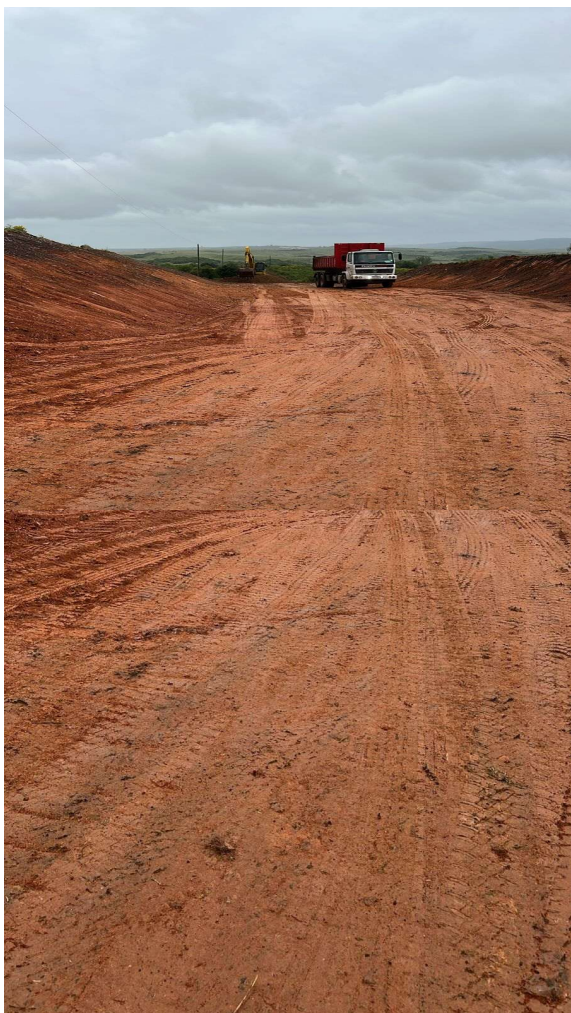


Três Estradas

❖ Timeline

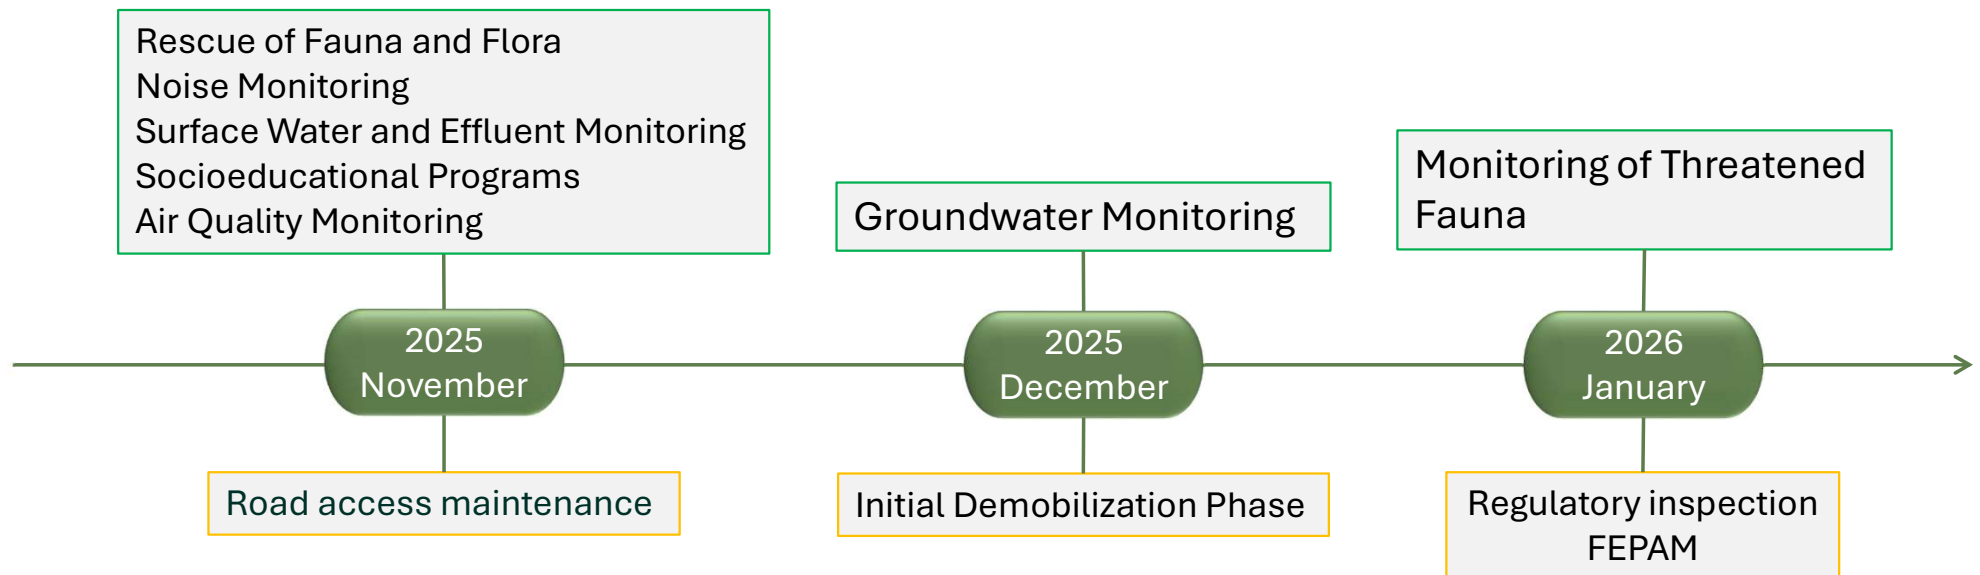


Três Estradas

❖ Timeline

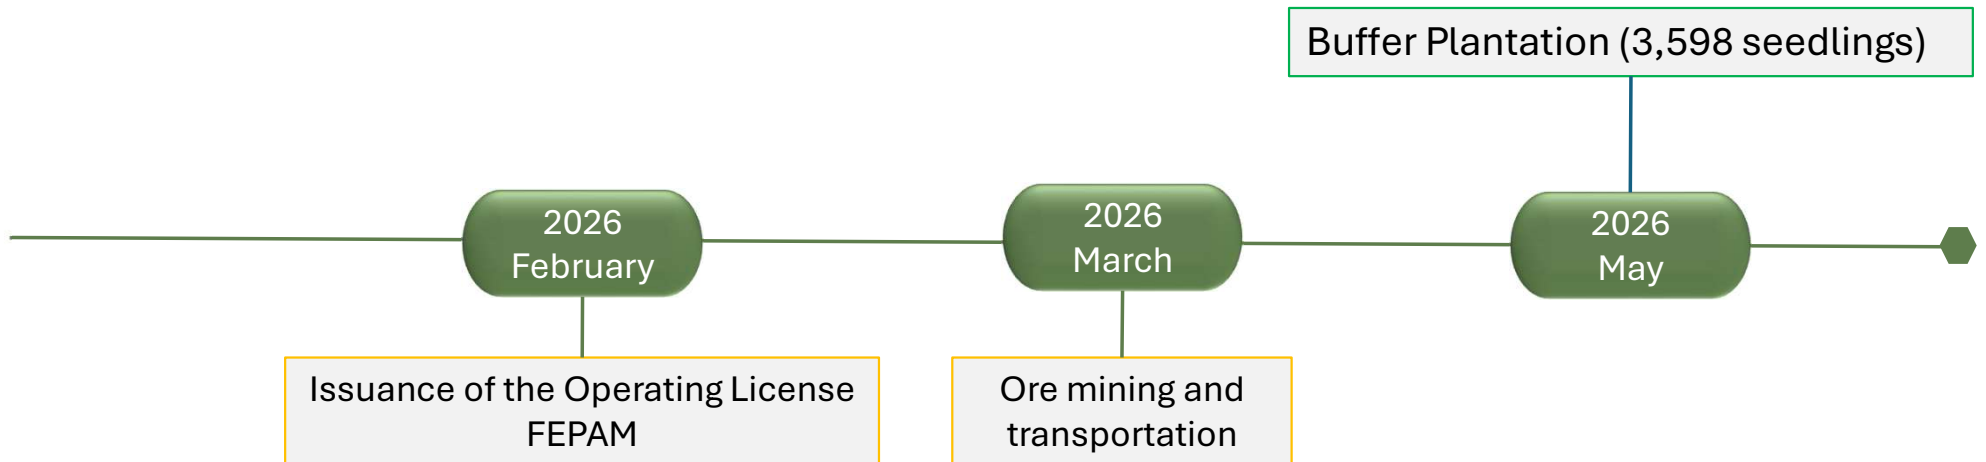

DBPlant

❖ Timeline

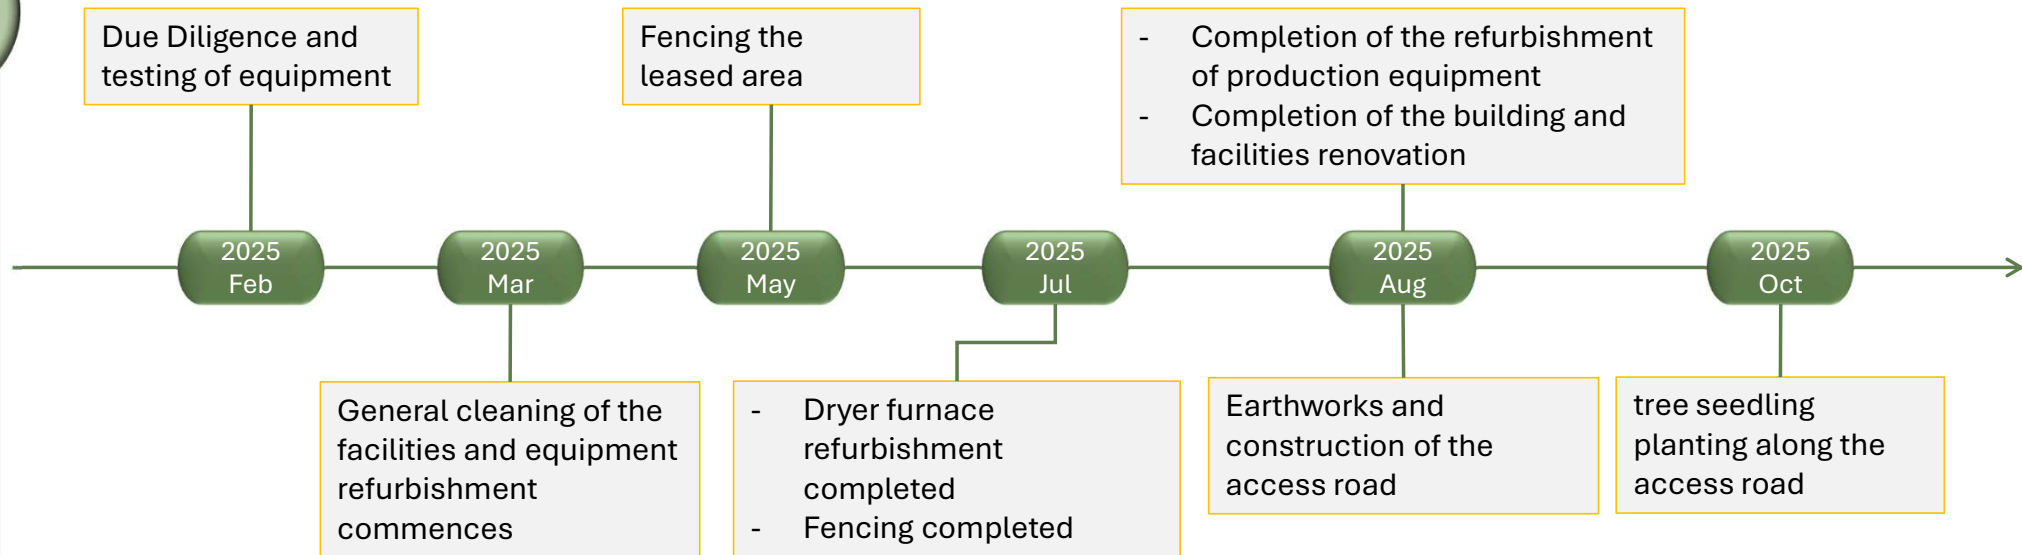

General cleaning of the facilities and equipment refurbishment

DBPlant

Timeline

2025
Mar

2025
Apr

2025
May

2025
Jun

2025
Jul

Rollers and bearings of the equipment

Before



After



Industrial cyclone separator

Before



After



General cleaning of the facilities and equipment refurbishment

DBPlant

Timeline



Support structure of the conveyor belt

Before



After



A vertical sidebar on the left side of the slide containing several icons: three location pins at the top, crossed hammers, a green circle with a factory icon, a shield with a plus sign, a caduceus, a target with an arrow, and a hand holding a coin.

General cleaning of the facilities and equipment refurbishment

DBPlant Timeline

- 2025 Mar
- 2025 Apr
- 2025 May
- 2025 Jun
- 2025 Jul

Before

After

Steel structure



DBPlant

Timeline

2025
Aug



DBPlant

❖ Timeline

Starter of civil works and installations

- RGE electrical grid connection
- Electric Power Substation + Medium Voltage Power Grid
- Road scale - civil works
- Modular Buildings (Containers)
- ROM stock shed (15X30)

2025
Nov

Signing of the purchase contract and commencement of manufacturing of the new production equipment

2025
Dec

Installation

- RGE electrical grid connection
- Electric Power Substation + Medium Voltage Power Grid

2026
Jan

Installation

- QGBT + 2 MCCs + 750 Kva Capacitor Bank

Installation

- Modular Buildings (Containers)
- Road scale
- ROM stock shed (15X30)

2026
Feb

Assembly of Equipment and platforms:

- Breaker + motor + metal base
- Hammer Mill + Motor
- Lung silo (hopper)
- Conveyor belts
- Bucket elevator
- Bag filter

2026
Mar

Assembly of Equipment:


- Big bag bagger (2 units)
- Bulk Loading Scale



DBPlant

❖ Production

2026 - Monthly production (tons/month)

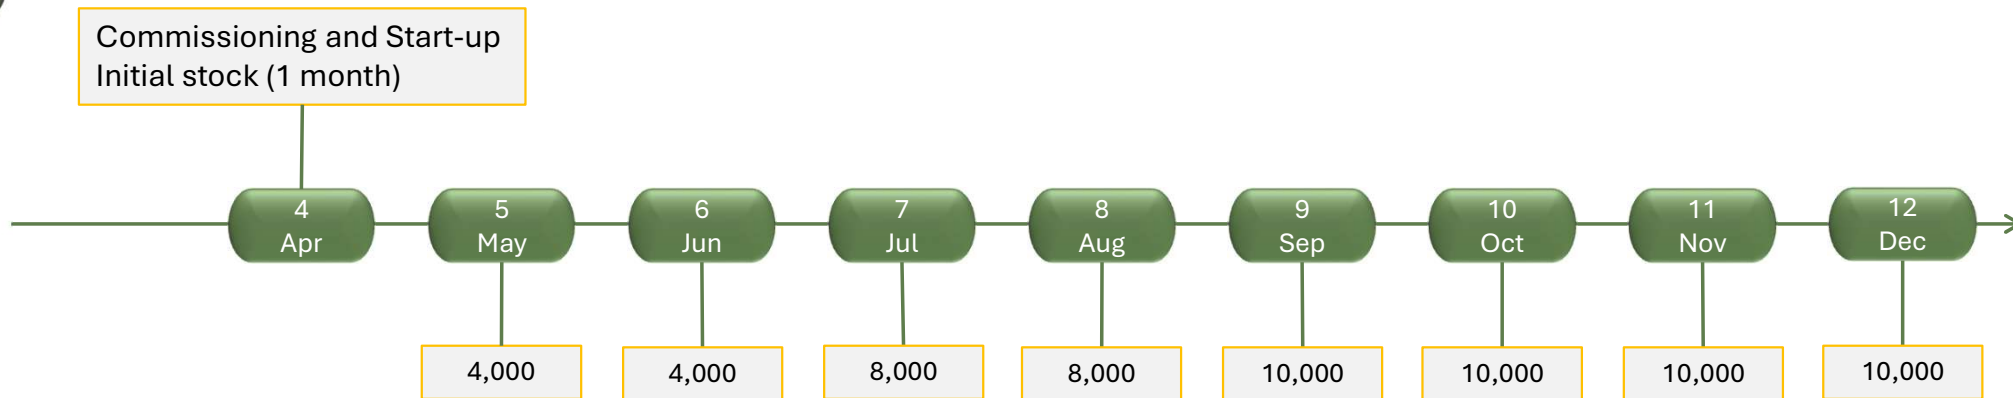

❖ Marketing





❖ Marketing

2025

Executed Memorandums of Understanding (MoUs)

54,000 tons



COTRISUL	5,000 t
FOLHITO	10,000 t
VETTORE	5,000 t
OCHOA	2,000 t
MULTI RURAL	2,000 t
AGPTEA	10,000 t
CAJU	10,000 t
3 ANNAS	10,000 t
total	54,000 tons

**Andean Mining Limited**

Offices of Corporacion Minera de
Colombia S.A.S.
Carrera 25 # 10 40 INT 2005 Medellín,
Antioquia, Colombia

Aguia Resources Limited

Level 12, 680 George Street
Sydney NSW 2000 Australia
+61 2 9375 7974 | +61 2 9287 0350
investor.relations@aguiaresources.com.au

**Aguia Fertilizantes S/A
Aguia Metais Ltda**

BR 392 KM 251
Caçapava do Sul / RS – Brazil
contato@aguiafertilizantes.com.br
